

TABLE OF CONTENTS

PARTI

PARTII

I. EXECUTIVE SUMMARY

II. RESULTS OF FIELD MONITORING BY PROJECT:

DISTRICT I

- CONSTRUCTION OF SANITARY LANDFILL, SUDIPEN
- 2 CONSTRUCTION OF SEPTAGE TREATMENT PLANT, BALAOAN
- 3 CONSTRUCTION OF COMPOSTING FACILITY, BALAOAN
- 4 COMPLETION OF THE REHABILITATION OF BURNOTAN COMMUNAL IRRIGATION SYSTEM (DAM), SAN GABRIEL
- 5 CONSTRUCTION OF BUGBUGCAO-PAGDILDILAN BRIDGE (PHASE I), SAN JUAN
- 6 CONSTRUCTION OF BUGBUGCAO-PACPACAC CREEK SLOPE PROTECTION, SAN JUAN
- 7 CONSTRUCTION OF CADACLAN SMALL WATER IMPOUNDING PROJECT (SITIO SURONG SECTION), CITY OF SAN FERNANDO
- 8 REHABILITATION AND IMPROVEMENT OF SAN VICENTE FARM TO MARKET ROAD, CITY OF SAN FERNANDO

DISTRICT II

- 9 COMPLETION OF COVERED COURT, UDIAO 185 ES, ROSARIO
- 10 CONSTRUCTION OF COVERED COURT (PHASE II), ALIPANG NHS, ROSARIO
- 11 CONSTRUCTION OF AMBANGONAN HANGING BRIDGE (PHASE II), PUGO
- 12 REHABILITATION, IMPROVEMENT AND UPGRADING OF STO. TOMAS-AGOO-TUBAO ROAD (AGOO SECTION) PHASE VII, AGOO
- 13 CONSTRUCTION OF MACABATO HEALTH CENTER, ARINGAY
- 14 REHABILITATION AND IMPROVEMENT OF CABA BEACH ROAD (PHASE II), CABA
- 15 CONSTRUCTION OF WATER SYSTEM, BAWANTA NHS, BAUANG
- 16 UPGRADING OF NAGUILIAN DISTRICT HOSPITAL BUILDING (TO INCREASE BED CAPACITY), NAGUILIAN

III. CONCLUSION

IV. MOVING FORWARD

I. ANNEXES

- LIST OF PARTICIPANTS DURING THE ACTUAL FIELD MONITORING
- 2 ATTENDANCE SHEET
- 3 COMMUNICATION LETTERS
- 4 PROVINCIAL PROJECT MONITORING COMMITTEE (PPMC) 4TH QUARTER 2024 ACTUAL FIELD MONITORING PROJECT DETAILS

EXECUTIVE SUMMARY

The Provincial Project Monitoring Committee (PPMC) conducted the 4th quarter actual field monitoring on December 5 and 11, 2024. The participants during the activity were as follows: Local Finance Committee (LFC) representatives from the Office of the Provincial Budget Officer (PBO), Office of the Provincial Accountant (OPAcctng) and Office of the Provincial Treasurer (PTO); Office of the Provincial Planning and Development Coordinator (OPPDC); and representatives from the implementing offices, which include the following: Office of the Provincial Agriculturist (OPAg), Provincial Health Office (PHO), PG Environment and Natural Resources Office (PG-ENRO), and Provincial Engineer Office (PEO).

A total of 16 infrastructure projects of various types were visited and assessed in order to evaluate the current status of projects as basis for future project improvement. Among the total projects monitored, nine projects were funded under RA 7171, three projects were funded under Special Education Fund (SEF), two projects were funded under Development Fund (DF), one project were funded under RA 8240 and one project under Trust Fund (TF).

This report contains the findings observed and their respective recommendations for each project visited for appropriate action of concerned offices.

During this quarter, the PPMC also assessed the conduct of the field monitoring and came up with opportunities for improvement for consideration in the future conduct of the activity such as the contractors must be informed of the project defects within the one-year defect liability period in order for them to perform the necessary repairs or address the concerns and shall be cascaded to and monitored by the PEO to be reported to the PPMC on a monthly basis.

CONSTRUCTION OF SANITARY LANDFILL, Sudipen

DEVELOPMENT FUND | Php 10,965,462.28

PROJECT DESCRIPTION

MAJOR

The project covers the construction of Cell w/ HDPE Liner, Leachate Pond, Storm Drainage and slope stabilization. The sanitary landfill has a total capacity of 2,500.00 cubic residual meters non-hazardous waste within a total effective area of 4,500.00 square meters and an estimated life span of 11 years. The project started on December 11, 2023 and was completed on October 14, 2024 which is ahead of its revised date of completion on October 21, 2024.

PROPOSED

ACTIONS TO BE **FINDINGS** TAKEN Performance of Contractors/Consultants Not fully compliant Comply with COA PEO/ with COA Circular Circular in Updating Contractor 2013-004 the Project billboard under "Information and Publication of PPAs Section 3.2 in Government Reporting and Monitoring. Agencies." Frequency and interval of verification is based from the approved Contract duration of the project. Legal and Policy Issuances

Environmental Compliance Certificate (ECC) was

posted on the project site.



ASSISTANCE TO LGUS IN THE ESTABLISHMENT OF WASTEWATER TREATMENT FACILITY (SEWERAGE, SEPTAGE, ETC), Balaoan


RA 7171 | Php 25,750,546.18

ROJECT DESCRIPTION

To address the worsening water quality and mitigate the sources of water pollution in the Province, this project aims to establish an LGUowned and managed septage treatment facility. This is directly aligned with the Sustainable Development Goal (SDG) No., 6.2, which aims for universal access to adequate equitable sanitation and hygiene for all, and SDG Goal No. 6.3 targets (1) water quality improved by 2030 by reducing pollution, eliminating dumping and minimizing release of hazardous chemicals and materials and (2) halving the proportion of untreated wastewater increasing and substantially recycling and safe reuse globally.

The project started on May 2, 2024 and is currently ongoing with 70 percent accomplishment as of December 31, 2024 and is expected to be completed on April 26, 2025.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | OPR |
|---|--|--------------------|
| Performance of Cont | ractors/Consultants | |
| Workers were not wearing complete Personal Protective Equipment (PPE) at the time of inspection | Provide/instruct workers to wear complete Personal Protective Equipment (PPE). | PEO/ Contractor |

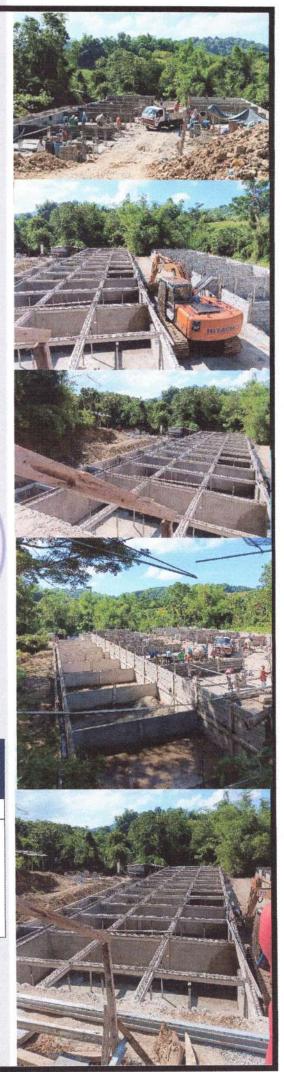

CONSTRUCTION OF COMPOSTING FACILITY, Balaoan

RA 7171 | Php 12,984,542.42

PROJECT DESCRIPTION

The project covers the construction of 15.00 meters x 8.00 meters Composting Facility with eight bed composting area, comfort room, bodega and working area. The project includes the concreting works, masonry works and roofing works. The project started on October 5, 2024 and was completed on December 18, 2024 which is ahead of its date of completion on February 1, 2025.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | OPR |
|--|---|------|
| Site Condition/Availa | bility | |
| The following areas are rough finished and not yet functional: -Comfort room -Bodega -Working area | Program additional funding for the completion of the project. | OPAg |
| No pathway leading to the facility | Include in the funding for the completion of the project. | OPAg |



COMPLETION OF THE REHABILITATION OF BURNOTAN COMMUNAL IRRIGATION SYSTEM (DAM), San Gabriel

RA 7171 | Php 8,760,197.30

PROJECT DESCRIPTION

The project covers the Continuation/ Completion of the Rehabilitation of the Burnotan Communal Irrigation System (DAM). The irrigation canal three distinct sections, spans covering a total length of 719 meters. The main dam, which is a key component of the system, is currently under construction and is funded by the National Irrigation Administration Region 1 (NIA-R1). Upon completion, the rehabilitated irrigation system will be fully operational. The project started on May 13, 2024 and was completed on January 13, 2025 which is ahead of its revised date of completion on January 28, 2025.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | 1850 OPR |
|---|--|--------------------|
| Performance of Cont | ractors/Consultants | |
| Not fully compliant with COA Circular 2013-004 "Information and Publication of PPAs in Government Agencies. | Comply with COA Circular in Updating the Project billboard under Section 3.2 Reporting and Monitoring. Frequency and interval of verification is based from the approved Contract duration of the project. | PEO/ Contractor |



CONSTRUCTION OF BUGBUGCAO-PAGDILDILAN BRIDGE (PHASE I), San Juan

RA 7171 | Php 9,735,355.20

The project covers the construction of 12.00 lineal meter bridge. During the course of the project, a Change Order was implemented, resulting in a modification from concrete railings to steel railings, along with the addition of stone masonry. This change was necessary due to the adjustment in the bridge's height and to suit the elevation of the creek. The construction started on November 9, 2023 and was completed on August 27, 2024 and which is on time from its revised completion date on August 28, 2024.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | OPR | |
|---|---|--------------------|--|
| Design, Scope, Techi | nical Specification | | |
| The bridge approach will be constructed on its Phase II | Program additional funding for the completion of the project. | PEO | |
| Performance of Cont | ractors/Consultants | | |
| Materials used such as sand and boulders have not yet been hauled | PEO to request the contractor for a site clearing. | PEO/ Contractor | |




1850

CONSTRUCTION OF BUGBUGCAO-PACPACAC CREEK SLOPE PROTECTION, San Juan

RA 7171 | Php 4,864,000.00

PROJECT DESCRIPTION

The project covers the construction of 86.00 lineal meter of Slope Protection with embankment. The project started on July 8, 2024 and was completed on September 4, 2024, which is ahead of its expected date of completion on December 4, 2024.

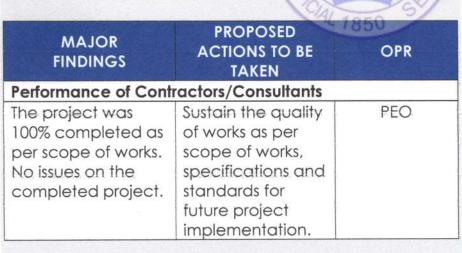



CONSTRUCTION OF CADACLAN SMALL WATER IMPOUNDING PROJECT (SITIO SURONG SECTION), City of San Fernando


RA 8240 | Php 4,872,050.25

PROJECT DESCRIPTION

The project covers the Construction of 5.00 meter x 8.00 meter x 1.50 meter Water Impounding Structure with four – 2.50 meter x 2.50 meter Weir and 15.00 meter x 3.00 meter Retaining Wall on both sides. The project started on April 19, 2024 and was completed on July 10, 2024, which is ahead of its completion date of September 15, 2024.

| MAJOR FINDINGS | ACHONS IO RE | |
|--|---|--------------------|
| Performance of Cont | ractors/Consultants | |
| The project was 100% completed as per scope of works. No issues on the completed project. Highly beneficial to the target beneficiaries. | Sustain the quality of works as per scope of works, specifications and standards for future project implementation. | PEO/ Contractor |

PROPOSED

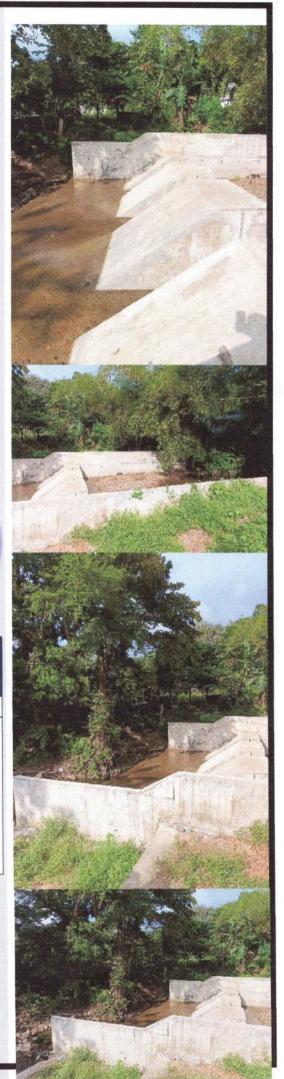

1850


REHABILITATION AND IMPROVEMENT OF SAN VICENTE FARM TO MARKET ROAD, City of San Fernando

RA 7171 | Php 3,998,458.20

ROJECT DESCRIPTION

The project covers the Rehabilitation and Improvement of 139.00 lineal meter Portland Concrete Cement Pavement and Provision of Drainage System. The project includes rail guard and stone masonry. The project started on May 22, 2024 was completed on December 4, 2024, which is ahead of its revised completion date on December 22, 2024.

| MAJOR ACTIONS TO BE TAKEN | | OPR |
|---|---|--------------------|
| Performance of Cont | ractors/Consultants | |
| The project was 100% completed as per scope of works. No issues on the completed project. | Sustain the quality of works as per scope of works, specifications and standards for future project implementation. | PEO/ Contractor |

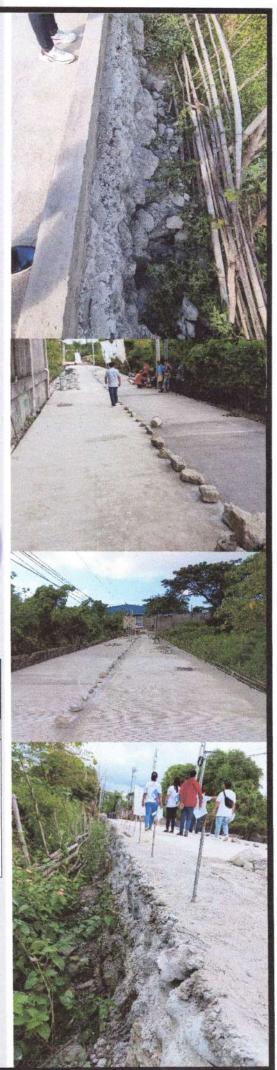

1850

COMPLETION OF COVERED COURT, UDIAO ES, Rosario

SPECIAL EDUCATION FUND | Php 2,489,225.15

ROJECT DESCRIPTION

The project covers the completion of cover court. The project covers the extension of existing roof and construction of Control Room. The project started on June 3, 2024 was completed on October 28, 2024, which is ahead the revised completion date on November 7, 2024.

| MAJOR FINDINGS | ACTIONS TO RE | |
|-------------------|-----------------------|------------|
| Performance of Co | ntractors/Consultants | |
| Minor cracks on | Repair affected | PEO/ |
| walls | areas | Contractor |



CONSTRUCTION OF COVERED COURT (PHASE II), ALIPANG NHS, Rosario

SPECIAL EDUCATION FUND | Php 2,491,564.12

ROJECT DESCRIPTION

The project covers the completion of covered court in Alipang National High School. The project involves the construction of stage and addition of 2-spans Covered Court with an area of 12.00 meter x 16.80 meter. The project started on June 3, 2024 and was completed on November 8, 2024, which is ahead of its completion date on November 22, 2024.



PROPOSED ACTIONS TO BE TAKEN

OPR

Performance of Contractors/Consultant

The project was 100% completed as per scope of works. No issues on the completed project. Highly beneficial to the target beneficiaries.

Sustain the quality of works as per scope of works, specifications and standards for future project implementation.

PEO/ Contractor



CONSTRUCTION OF AMBANGONAN HANGING BRIDGE (PHASE II), Agoo

RA 7171 | Php 6,818,000.00

PROJECT DESCRIPTION

The project covers the construction of Hanging Bridge with total length of 99.50 lineal meter steel bridge. The project includes the construction of 120.62 cubic meter stone masonry, 520.00 cubic meter gabion and installation of lighting fixtures. The project started on July 8, 2024 and was completed on October 15, 2024, which is ahead of its target completion date of November 4, 2024. OF

PROPOSED MAJOR **ACTIONS TO BE** OPR **FINDINGS** TAKEN Performance of Contractors/Consultant The project was Sustain the quality PEO/ 100% completed as of works as per Contractor per scope of works. scope of works, No issues on the specifications and completed project. standards for Highly beneficial to future project the target implementation. beneficiaries.





REHABILITATION, IMPROVEMENT AND UPGRADING OF STO. TOMAS-AGOO-TUBAO ROAD (AGOO SECTION) PHASE VII, Caba

RA 7171 | Php 4,867,700.00

PROJECT DESCRIPTION

The project covers the improvement of 130.00 meter Portland Concrete Cement Pavement with 60.00 lineal meter x 6.00 meter Stone Masonry. The project started on May 2, 2024 and was completed on October 25, 2024, which is ahead of its revised completion date on October 28, 2024.

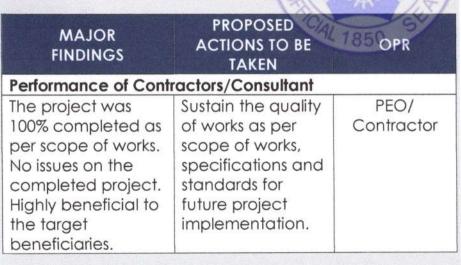

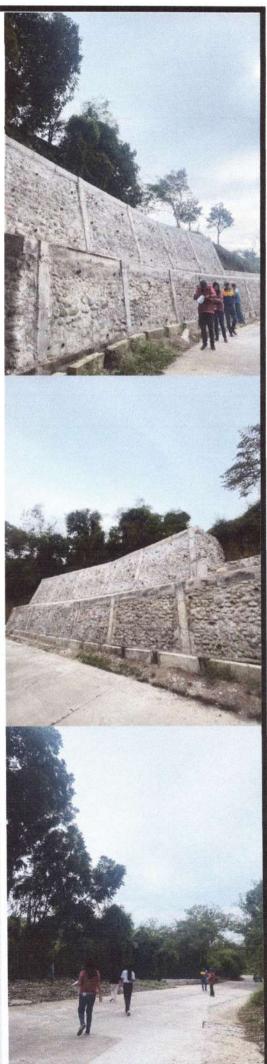

CONSTRUCTION OF MACABATO HEALTH CENTER, Aringay

RA 8240 | Php 9,229,547.95

PROJECT DESCRIPTION

The project covers the completion of two-storey Health Center. The Phase I of the project implemented by the was Department of Public Works and Highways (DPWH). The project includes removal of structures and obstructions, construction of septic tank, plumbing works, ceiling works, installation of doors and windows, electrical works, painting works and tiling works. The project started on May 13, 2025 and was completed on March 12, 2025, which is on time with its revised completion date on March 13, 2025.

MAJOR FINDINGS

PROPOSED ACTIONS TO BE TAKEN

Performance of Contractors/Consultants

The plumbing rough-in for some water closets was positioned too far from the wall, resulting in a noticeable gap between the wall and the tank.

Adjust the placement of the water closet to ensure proper alignment and prevent potential accidents

Contractor, PEO

Others

Plumbing and electrical rough-ins were not included in Phase I. As a result, PEO decided to leave the electrical wires exposed, covering them with moulding, and allow certain plumbing pipes to remain visible. This approach was chosen to minimize additional costs associated with extensive wall chipping and tile removal.



DESCRIPTION

Rehabilitation and Improvement of Caba Beach Road (Phase II), Caba

RA 7171 | Php 4,859,107.55

project The covers the rehabilitation of 250.00 lineal meter Portland Cement Concrete Pavement with varying widths ranging from 6.20-7.00 meter and a thickness of 0.28 meter. The project started on April 16, 2024 and was completed on October 25, 2024, which is on time with its revised completion date.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | OPR |
|---|---|--------------------|
| Performance of Cont | ractors/Consultants | |
| Transverse crack located within the middle third of the block was noted on the completed pavement | Seal the noted transverse crack located within the middle third of the PCCP block with pressurized concrete epoxy | Contractor, PEO |
| Some parts of the road joints have no sealant | Apply sealant to any joints that are unsealed. | |



1850

CONSTRUCTION OF WATER SYSTEM, **BAWANTA NHS, Bauang**

SPECIAL EDUCATION FUND | Php 1,996,056.14

The project covers the construction of potable water system and provision of water supply at school project includes office. The installation of two 1.5 horsepower water pump and 1 unit 2000 liter water tank The project started on June 3, 2024 and was completed on July 26, 2024, and which is ahead from its expected completion date on August 1, 2024.

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | OPR |
|---|---|--------------------|
| Performance of Cont | ractors/Consultants | |
| Faucets in the handwash area are not dispensing water | Repair the waterline to make the handwash area functional | PEO/ Contractor |




UPGRADING OF NAGUILIAN DISTRICT HOSPITAL BUILDING (TO INCREASE BED CAPACITY), Naguilian

TRUST FUND | Php 49,972,946.71

PROJECT DESCRIPTION

The project covers the construction of three-storey building with service roofdeck. This phase includes the finishing of its ground floor with installed CCTV-Network-Telephone Equipment and Fire Detection and Alarm System. The ground floor consists the two Operating Rooms, Delivery Room with Labor Room, Recovery Room, Nurse Station, Lounge Doctors' and other Amenities, OB-GYNE Ward, and Surgical Ward. The project started on December 6, 2022 and was completed on October 10, 2024, which is ahead from its revised completion date October 25, 2024. 1850

| MAJOR FINDINGS | PROPOSED ACTIONS TO BE TAKEN | S OPR |
|---|---|--------------------|
| Performance of Cont | ractors/Consultants | |
| The project was 100% completed as per scope of works. No issues on the completed project. | Sustain the quality of works as per scope of works, specifications and standards for future project implementation. | PEO/ Contractor |

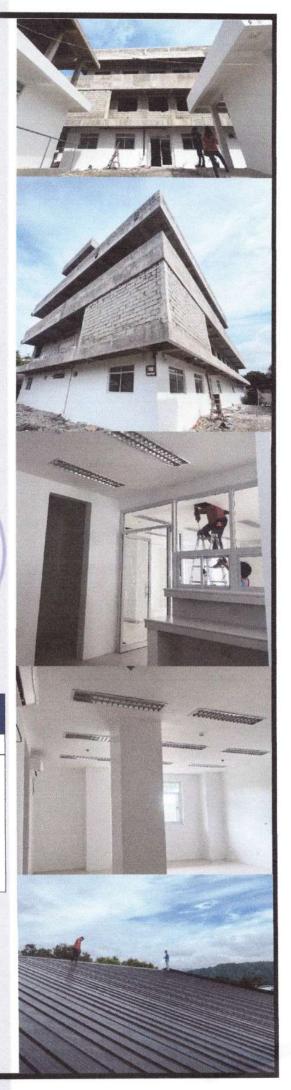

CONCLUSION

A total of 16 infrastructure projects were visited during the 4th quarter 2024 actual field monitoring activity on December 5 and 11, 2024. All enlisted projects were monitored accordingly and the monitoring team managed to accurately assess and evaluate the projects visited. Among the common findings observed were as follows:

- Workmanship of most projects visited were commendable;
- Few of the projects visited were already being used and received positive feedback from beneficiaries/end-users;
- For the completed projects, the end users were informed of their role to maintain the structure's cleanliness, usability and structural integrity;
- For the ongoing projects to be completed within their target duration of implementation; and
- Some projects have minor structural damages that need to be repaired by the contractor;

With the above enumerated findings, the resident Engineers of the PGLU have been initially informed during the actual field monitoring for appropriate action. The PPMC will ensure that actions to be taken shall be done accordingly by the contractor in coordination with the implementing office/s. A monitoring report of the actions taken by the concerned offices shall be prepared during the succeeding quarter (Q1 2025).

MOVING FORWARD

To enhance future project implementation and as per agreement during the post-assessment of the conduct of the 4th Quarter 2024 Actual Field Monitoring activity, the Monitoring Team has reiterated the following general recommendations:

- Sustain the quality of works as per scope of works, specifications and standards;
- COA Billboard must be updated monthly to ensure transparency of the status or progress of the on-going project/s;
- Strict compliance in the use of PPE must be imposed and monitored; and
- The contractors must be informed of the project defects within the one-year defect liability period in order for them to perform repairs / address the concerns. This shall be cascaded through the PEO and shall be monitored by the PPMC.



PROJECT MONITORING COMMITTEE

MICHAELA LOUIS D. JAVIER, EnP, MM
PPMC Head Secretariat

REMIGIO S. BONIFACIO III
PPMC Chairperson



Date of Monitoring: December 5, 2024

Participants:

| Mr. Remigio S. Bonifacio III | PPMC Chairperson |
|------------------------------|------------------|
| | |

Represented by: Mr. Kyle Aungon

EnP Julie Ann A. Arciaga OPPDC

Engr. Kathrina Manipon OPPDC

Atty. Evelyn Obra OPAcc

Ms. Marzel L. Hufana PTO

Mr. John Benedict C. Marasigan PG-ENRO

Ms. Myrna Balanon OPAg

Mr. Mario Obra OPAg

Mr. Mamerto A. Directo OPAg

Ms. Alma Ordinario OPAg

Mr. Noel Mendoza OPAg

Mr. Reynaldo Balala

Mr. Michael Licay

Engr. Michael A. Manzano

Engr. Jomar Hufana PEO

Engr. Bernadine Louise Olbinado 1850 PEO

Engr. Glen Fray Fernandez PEO

Paul Joffrey Ramirez LGU-Balaoan

ATTENDANCE SHEET

Activity: Actual Filed Monitoring

Date: December 5, 2024

| 1 2 | NAME | M | - | | | |
|-----|-------------------------|---|--|-------------|-------------|-------------|
| | | | F | AGENCY | NUMBER | SIGNATURE |
| 2 | John poenedia o Maragan | / | | PG-ENRO | 19457831245 | pocuonansur |
| 2 | Marzel Hufana | | / | PTO | | may |
| 3 | Evelyn Obra | | / | Accts | | - ADD- |
| 4 | UDMAR HUFAHA | / | | PEO | | you. |
| 5 | BERMOINE LOUGE OLE NADO | | 18 | 260 | | DA |
| 6 | KYLE ANTIGON | 1 | | CF-03/1 | | Charles |
| 7 | SEM PHAY PETHANDEL | / | | िह्य | | - 25 |
| 8 | PAUL JOFFREY KAMINER | / | | LGU-BALADAN | | |
| 9 | MyEN ARME | _ | , | PPDO | < | 1 Kg |
| 10 | myrina maranin | | \checkmark | OVEC | | VA & |
| 11 | MADIO OBY | / | | PURCH peto | | orga |
| 12 | MAMERO O. DIRECTO | 1 | | OPA6 | | of. |
| 13 | ALMY ORDINARIO | | - | OPAGOF) | | A hy |
| 14 | NOEL MENDOZA | / | 13 | OPA 6 | 3 | Long |
| 15 | REMALDO BALALA | / | 6 | PA6 | Z | de A |
| 16 | MICHAEL LICAY | 1 | œ/ | OPAC | 101 | and |
| 17 | KATHRINA MANIPON | | | OPPDC | Z | K |
| 18 | MICHAEL MANZAND | - | 0 | Pa | | 0 |
| 19 | Jule am arrian | | 130 | 08806 | 15 | 1 |
| 20 | Tricia Mea Carpio | | 1 | 0000C | 5 | (19) |
| 21 | Michelle Garcia | | 1 | 06625 | | 40 Fey |
| 22 | Kimberly Alicha | | 1 | OPPDC | | 1 6.5 |
| 23 | Jomarny Hipolito | / | Þ | 27990 | | 4 |
| 24 | Edna Hernandez | - | 1 | 06600 | | 16h |
| 25 | Painier De Guzman | / | of the same of the | 06600 | | 40 |
| 26 | du co cio sunti | | | - 1(0 | | |
| 27 | 0, | | | | | ~ |
| 28 | | | | | | |
| 29 | | | | | | |
| 30 | | | | | | |
| 31 | | | | | | |
| 32 | | | | | | |
| 33 | | | | | | |
| 34 | | | | | | |
| 35 | | | | | | |

Certified Correct:

JACK TO THE CONTROL OF THE CONTROL O

Date of Monitoring: December 11, 2024

Participants:

Mr. Remigio S. Bonifacio III PPMC Chairperson

Dir. Reggie R. Colisao PPMC Member Represented by: Engr. Ariel Zamoranos

Mr. Jumel P. Tabucol PPMC Member Represented by: Mr. Kurt Russel D. Marcial

Hon. Magno A. Wailan, C.E. PPMC Technical Partner

Represented by: Engr. Francisco P. Areola

1850

Engr. Kathrina Manipon OPPDC

Ms. Tricia Mea B. Carpio, LPT OPPDC

Atty. Evelyn Obra OPAcc

Ms. Marzel Hufana PTO

EDE

Engr. Michael Manzano PEO

Engr. Dean Trojan Alcantara PEO

Engr. Gladys Kate Lipawen PEO

Engr. Bernadine Louise Olbinado PEO

Engr. Julius Gurtiza PEO

ATTENDANCE SHEET

Activity: Actual Filed Monitoring

Date: December 11, 2024

| NO | NAME | SEX | | OFFICE/ | CONTACT | SIGNATURE | |
|-------|--|-----|-----|-----------|-------------|------------|--|
| 10.72 | and the state of t | M | F | AGENCY | NUMBER | SIGNATURE | |
| 1 | Kurt Russel D. Marcial | / | | LINK | 09950013759 | parying | |
| 2 | Marzel Aufana | | / | PTO | | (all | |
| 3 | BALLE GENERA | 14 | | PRO | | | |
| 4 | Record Vadonnes | | | | | Just | |
| 5 | Gladys kate Lipawen | | 1 | PTO | 1 | | |
| 6 | Bernodine abinado | | 1 | PEO | | Den C | |
| 7 | Michael Hanzana | 1 | | PED | | | |
| 8 | JULIUS GURITA | / | | PEO | | 4 | |
| 9 | trulen dora | | / | Acch | | 17/100 | |
| 10 | DEAN ALCANTARA | / | | PECO | | 100 | |
| 11 | Kathrina Manipon | | 1 | OPPUC | | Said | |
| 12 | Tricia Mea Curpio | | / | OPPUC | | A for you | |
| 13 | Moyer Avaya | / | | COPHOCE) | | // / | |
| 14 | REMIGIO S. BONIFACIOI | 11/ | 13 | CREBA | 4 | 1 | |
| 15 | FRANCISCO P. AREOLA | 1 | 6 | PICE | Z | res | |
| 16 | ARIEL ZAMORANOS | 1 | 02/ | DILO LU | 10 | / 0 | |
| 17 | Kimberly alicea | | | OPPOC | Z / | į. | |
| 18 | Jean argallion | 1 | 3 | OPPDG | | Finds | |
| 19 | Charles abenoja | | 1 | Oppoc | 150 | 18 | |
| 20 | Edna Hernandez | | 1 | A/OPPOCED | 5 | Alenga | |
| 21 | faineir De Guznan | 1 | | OPPDO | | Ko | |
| 22 | Abdinar Yaranon | 1 | | | | Dynein | |
| 23 | annie Taturay | | 1 | | | - Thirtmay | |
| 24 | Lelia Dilay | | / | | | Leciapung | |
| 25 | Frederita Ubaldo | | 1 | | | Fredelita | |
| 26 | | | | | | | |
| 27 | | | | | | | |
| 28 | | | | | | | |
| 29 | | | | | | | |
| 30 | | | | | | | |
| 31 | 17 17 17 17 17 17 17 17 17 17 17 17 17 1 | | | | | | |
| 32 | | | | | | | |
| 33 | | | | | | | |
| 34 | | | | | | | |
| 35 | | | | | | | |

Certified Correct:



The Heart of Agri-Tourism in Northern Juzon by 2025 OFFICE OF THE GOVERNOR



November 25, 2024

REMIGIO S. BONIFACIO III

President, Chamber of Real Estate and Builders
Association, Inc.-La Union Chapter and
Chairperson, Provincial Project Monitoring Committee (PPMC)
2nd Floor, Eso-Nice Bldg. Gov. Luna St.,
City of San Fernando, La Union

Dear Mr. Bonifacio:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as the chairperson of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.ly/4thQtt2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may confact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Union.

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID

Provincial Governor

Enclosure: as stated (1 page)

CHEN HENDORN CON-

12-04-2027

ADM-048-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

(072) 888-3608. (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph

@ www.launion.gov.ph

Seal of Good Local Governance







The Heart of Agri-Tourism in Northern Juzon by 2025



November 25, 2024

adda pay mayor may clo MEU-(Kat)

REGGIE R. COLISAO, CESO V

Provincial Director, DILG-La Union/ Member, Provincial Project Monitoring Committee (PPMC) Aguila Rd., Brgy. Sevilla, City of San Fernando, La Union

Dear Dir. Colisao:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.ly/4thQtr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capital Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or atmobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Union,

Provincial Governor A

Enclosure: as stated (1 page)

MAUNION & LEASE OF THE MAIN OF THE PROPERTY OF

ADM-048-0

GOD-LOVING PEOPLE-ORIENTED ACCOUNTABLE COMMITTED PROVINCIAL CAPITOL OF SAIN FEMALOD, 2500 La Unión (072) 888-3608: (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph

www.launion.gov.ph

Seal of Good Local





Pagkilala Sa Katapatan at Kahucayan ng Pansahataang Lokal

Performance Governance System

Quality Management System



"The Heart of Agri-Tourism in Northern Juzon by 2025



OFFICE OF THE GOVERNOR

November 25, 2024

JUMEL P. TABUCOL

President, Lupon ng mga Indibidwal na Nangangalaga sa Kalikasan, Inc. (LINK) 3rd Floor, Marcos Bldg., San Fernando City, La Union

RECEIVED LUPON NG MGA INDIBIDWAL NA NANGANGALAGA NG KALIKASAN, INC. 12/02/24

Dear Mr. Tabucol:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.ly/4th@tr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathring Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Union.

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID Provincial Governor

Enclosure: as stated (1 page)

Y, ALFREDO PABLO R. ORTEGA, MNSA CITY VICE WAYOR

DAME ROUNTS

11: Cram

ADM-048-0

00-2024-11-125

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

(072) 888-3608; (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph

www.launion.gov.ph

eal of





ning Pomahalkang Lokal



"The Heart of Agri-Tourism in Northern Juzon by 2025 OFFICE OF THE GOVERNOR



November 25, 2024

ADRIAN GABRIEL S. GO

President, Rotary Club of San Fernando (LU), Inc. 3rd Floor Josefina Bldg., Rizal Ave., Brgy. III, City of San Fernando, La Union

Dear Mr. Go:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.ly/4thQt/2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Union,

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID

Provincial Governor

Enclosure: as stated (1 page)

beauth his

12-04-2024

ADM-048-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED (072) 888-3608; (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph







"The Heart of Agri-Tourism in Morthern Juzon by 2025 OFFICE OF THE GOVERNOR



November 25, 2024

ARCH. RONALD S. DY

President, Filipino - Chinese Chamber of Commerce & Industry of La Union Inc. (FCCCILU) c/o Colorado Graphix, Quezon Ave., National Highway, Sevilla, City of San Fernando, La Union

Dear Arch. Dy:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.lv/4thQtr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capital Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Unione

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID

Provincial Governor

Enclosure: as stated (1 page)

OWN LIMENDOSM

ADM-048-0

GOD-LOVING * PEOPLE-ORIENTED * ACCOUNTABLE * COMMITTED 2nd Floor, Provincial Capitol, City of San Fernanco, 2500 La Union (072) 888-3608 (072) 888-6035 * (072) 888-4453

(072) 888-3608; (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph

www.launion.gov.ph







Performance Governance System

Quality Management System



"The Heart of Agri-Tourism in Morthern Juzon by 2025 OFFICE OF THE GOVERNOR



November 25, 2024

HON. MAGNO A. WAILAN, CE

Municipal Mayor and President,

Philippine Institute of Civil Engineers (PICE), Inc. – La Union Chapter
Mayor's Office, Municipality of Santol, La Union

Dear Mayor Wailan:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit.ly/4thQtr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Dios ti agngina.

God bless us all and God bless our fair La Union,

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID

Provincial Governor

Enclosure: as stated (1 page)

ANABELLE G. CASUGA DEC. 02, 2024

ADM-048-0

GOD-LOVING PEOPLE-ORIENTED ACCOUNTABLE COMMITTED 2nd Floor, Provincial Capitol, City of San Fernanco, 2500 La Union (072) 888-3608; (072) 888-6035 (072) 888-4453 govrafy@launion.gov.ph









Performance Governance System

Quality Management System



The Heart of Agri-Tourism in Northern Juzon by 2025



OFFICE OF THE GOVERNOR

MEMORANDUM NO. 463 S. 2024

PGLU ACCOUNTING ANCEIVED BY: -

.37 Ate.

12/03/24

TO

: MS. CATHERINE E. FRANCO, Provincial Budget Officer - Machine

ATTY. ALBERT F. PADILLA, Provincial Accountant

MS. JANET D. MOLINA, Provincial Treasurer - mm 12/2/2/20

SUBJECT

: CONDUCT OF 4TH QUARTER 2024 ACTUAL PROJECT MONITORING

ACTIVITY TO SELECTED DEVELOPMENT PROGRAMS AND PROJECTS OF

PGLU

DATE

: November 25, 2024

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, as a member of the PPMC, may we invite you for the conduct of the 4th Quarter Actual Field Monitoring Activity on December 5 and 11, 2024. Please confirm your attendance at bit 1/4thQtr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Your attendance and active participation in the said activity is earnestly requested.

Dios ti agngina.

RAPHAELLE VERONICA "RAFY" ORTEGA-DAVID

Provincial Governor

Enclosure: as stated (1 page)

ADM-048-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

Floor, Provincial Capitol, City of San Fer (072) 888-3608; (072) 888-6035 (072) 888-4453

govrafy@launion.go

mww.launion.gov.ph

Seal of Good governance





Pagkitata Sa Katapatan at Kahutayan ng Pamahatxang Lokaf



The Heart of Agri-Tourism in Morthern Juzon by 2025 OFFICE OF THE PROVINCIAL PLANNING AND DEVELOPMENT COORDINATOR



November 25, 2024

PPDO THE

MS. SHARON A. VILORIA

Office-In-Charge
Office of the Provincial Agriculturist
Province of La Union

11-26

Dear Ms. Viloria:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), (2) RA 7171 Fund, (3) RA 8240 Fund, and (4) Special Education Fund (SEF).

In this regard, may we respectfully invite you or your authorized representative to attend the 4th Quarter Actual Field Monitoring Activity, which includes the monitoring of the projects, Construction of Cadacian Small Water Impounding Project (Sitio Surong Section), City of San Fernando and Construction of Composting Facility, Balaoan on December 5, 2024. Please confirm your attendance at bit ly/4th and place is 8:00 a.m. at the Provincial Capitol Lobby.

For further inquiries, you may contact Engr. Kathrina Manipon. Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. [072] 242-5550 loc. 232 or at mobile number 09260096547.

Thank you very much.

Respectfully yours,

ATTY. RUBY JEAN N. BALANON, EnP
Acting Provincial Planning and Development Coordinator

PPDC-001A-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

@ www.launion.gov.ph

(072) 242-5550;

(072) 700-4764

glu_ppdo@launion.gov.ph

Perfective in Ketigratur et Kananasse og Famabalasse, inke PGS



a Katapatan et Prokoman e Sevenario Syr

version lyden. Quality Manager



The Heart of Agri-Tourism in Northern Juzon by 2025 Office of the provincial planning and DEVELOPMENT COORDINATOR



PPDO FILE

November 25, 2024

ANNALYN ROSARIO-VALDEZ, EnP
PG Environment and Natural Resources Officer

Province of La Union

Dear EnP Rosario-Valdez:

Angela 11/27/2024 10-Ento

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), (2) RA 7171 Fund, (3) RA 8240 Fund, and (4) Special Education Fund (SEF).

In this regard, may we respectfully invite you or your authorized representative to attend the 4th Quarter Actual Field Monitoring Activity, which includes the monitoring of the projects, Construction of Sanitary Landfill, Sudipen and Construction of Septage Treatment Plant, Balaoan on December 5, 2024. Please confirm your attendance of an Actual 2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capital Labby.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 231 or at mobile number 09260096547.

Thank you very much.

1850

Respectfully yours,

ATTY. RUBY JEAN N. BALANON, EnP
Acting Provincial Planning and Development Coordinator

PPDC-001A-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

(072) 242-5550. (072) 700-4784 pglu_ppdo@laumon.gov.ph

mww.launion.gov.ph

Seal of Good Governance

ernance



Prefamiliar de Governance Systems

Quality Missagement System



The Heart of Agri-Tourism in Northern Juzon by 2025 OFFICE OF THE PROVINCIAL PLANNING AND DEVELOPMENT COORDINATOR



November 25, 2024

PPDO FILE

DR. HERMINIGILDO M. VELASCO Provincial Health Officer Province of La Union Many

Dear Dr. Velasco:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), (2) RA 7171 Fund, (3) RA 8240 Fund, and (4) Special Education Fund (SEF).

In this regard, may we respectfully invite you or your authorized representative to attend the 4th Quarter Actual Field Monitoring Activity, which includes the monitoring of the projects, Construction of Macabato Health Center, Aringay on December 11, 2024. Please confirm your attendance at bit.ly/4thQtr2024-AFM-Confirmation on or before December 2, 2024. The assembly time and place is 8:00 a.m. at the Provincial Capitol Lobby.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232 or at mobile number 09260096547.

Thank you very much.

1850

Respectfully yours,

ATTY. RUBY JEAN N. BALANON, EnP
Acting Provincial Planning and Development Coordinator

PPDC-001A-0

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

(072) 242-5550. a pglu_ppdo@lau (072) 700-4764

www.launion.gov.ph

Seal of Good local agvernance

Settingual p





Podomaco Soverhano system

Quality Management System



The Heart of Agri-Tourism in Northern Juzon by 2025 OFFICE OF THE PROVINCIAL PLANNING AND DEVELOPMENT COORDINATOR



November 25, 2024

ENGR. RESSIE A. ESTRELLA

Provincial Engineer
Provincial Government of La Union

PPDO FILE

Dear Engr. Estrella:

As per mandate of providing basic information on the implementation status of development programs and projects as well as strengthening the monitoring and evaluation system of the Provincial Government of La Union (PGLU), the Provincial Project Monitoring Committee (PPMC) regularly conducts actual site visits to the different projects initiated under the (1) Development Fund (DF), and (2) RA 7171 Fund, (3) Special Education Fund, (4) RA 8240 Fund, and (5) Trust Fund (TF).

In this regard, may we request the presence of your concerned Resident Engineers during the scheduled 4th Quarter 2024 project monitoring on **December 5 and 11**, **2024**. The assembly time and place is **8:00 a.m. at the Provincial Capitol Lobby**. In addition, kindly provide the Office of the Provincial Planning and Development Coordinator (OPPDC) with the latest and updated documents needed for the said activity such as the Program of Work (POW), Statement of Work Accomplishment (SWA), Change Order, Computation of Time Elapsed, original and revised Detailed Engineering Drawings (DED) and Project Phasing Diagram/Map (for multiple phased projects) on or before **December 2**, **2024** to be used as reference during the said activity. Attached is the list of projects to be monitored for your reference and perusal.

For further inquiries, you may contact Engr. Kathrina Manipon, Project Evaluation Officer I of the Office of the Provincial Planning and Development Coordinator (OPPDC) at tel. no. (072) 242-5550 loc. 232.

Thank you very much.

Respectfully yours,

ATTY. RUBY JEAN N. BALANON, ENP

Acting Provincial Planning and Development Coordinator

Enclosure: as stated (1 page)

PPDC-001A-0 OC-2024-11-094

GOD-LOVING . PEOPLE-ORIENTED . ACCOUNTABLE . COMMITTED

) 242-5550: (072) 700-4764 a pglu_ppdo@leunion.gov.ph

www.launion.gov.ph








Depletate Sa Katopatian of Katopowan ng Pannakakong rekak Portionance September System

Lates Management Septem

| | | ECT MONITORING (ACTUAL FIELD M | COMMITTEE (PPMC) ONITORING | 1 | |
|----------------|--|---------------------------------|-------------------------------|-----------|---------|
| LOCATION | PROJECT NAME | COST OF APPROVED BUDGET | CONTRACT COST | STATUS | FUND |
| SUDIPEN | Construction of Sanitary Landfill | 11,000,000,00 | 10,965,462,28 | Ongoing | DF |
| BALAOAN | Construction of Septage Treatment Plant | 25,800,000.00 | 25,750,546.18 | Ongoing | DF |
| | Construction of Composting Facility | 1,000,000.00 | | Ongoing | RA 7171 |
| SAN GABRIEL | Completion of the Rehabilitation of Burnotan Communal Irrigation System (Dam) | 8,775,000.00 | 8,760,197.30 | Ongoing | RA 7171 |
| | Construction of Bugbugcao-Pagdildilan Bridge (Phase I) | 9,750,000.00 | 9,735,355.20 | Completed | RA 7171 |
| SAN JUAN | Construction of Bugbugcao-Pacpacac Creek Slope Protection | 4,875,000.00 | 4,864,000.00 | Completed | RA 7171 |
| CITY OF | Construction of Cadaclan Small Water Impounding Project (Sitio Surong Section) | 3,000,000.00 | 2,997,709.73 | Completed | RA 7171 |
| FERNANDO | Rehabilitation and Improvement of San Vicente Farm to Market Road | 4,000,000.00 | 3,998,458.20 | Ongoing | RA 7171 |

| PROVINCIAL PROJECT MONITORING COMMITTEE (PPMC) 4 TH QTR 2024 ACTUAL FIELD MONITORING December 11, 2024 (DISTRICT H) | | | | | | | | | |
|--|--|-------------------------------|---------------|-----------|----------------|--|--|--|--|
| LOCATION | PROJECT NAME | COST OF APPROVED BUDGET | CONTRACT | STATUS | FUND SOURCE | | | | |
| ROSARIO | Completion of Covered Court, Udiao ES | 2,500,000,00 | 2,489,225.15 | Ongoing | SEF | | | | |
| ROSARIO | Construction of Covered Court (Phase II), Alipang NHS | 2,500,000,00 | 2,491,564.12 | Ongoing | SEF | | | | |
| PUGO | Construction of Ambangonan Hanging Bridge (Phase II) | 6.825,000.00 | 6,818,000.00 | Completed | RA 7171 | | | | |
| AGOO | Rehabilitation, Improvement and Upgrading of Sto. Tomas-Agoo-Tubao Road (Agoo Section) Phase VII | 4,875,000.00 | 4,867,700.00 | Ongoing | RA 7171 | | | | |
| ARINGAY | Construction of Macabato Health Center | 9,233,058.90 | 9,229,547.95 | Ongoing | RA 8240 | | | | |
| CABA | Rehabilitation and Improvement of Caba Beach Road (Phase II) | 4,875,000.00 | 4,859,107.55 | Ongoing | RA 7171 | | | | |
| BAUANG | Construction of Water System, Bawanta NHS | 2,000,000.00 | 1,996,056.14 | Completed | SEF | | | | |
| NAGUILIAN | Upgrading of Naguilian District Hospital Building (To Increase Bed Capacity) | 50,000,000.00 | 49,972,946.71 | Completed | TF | | | | |

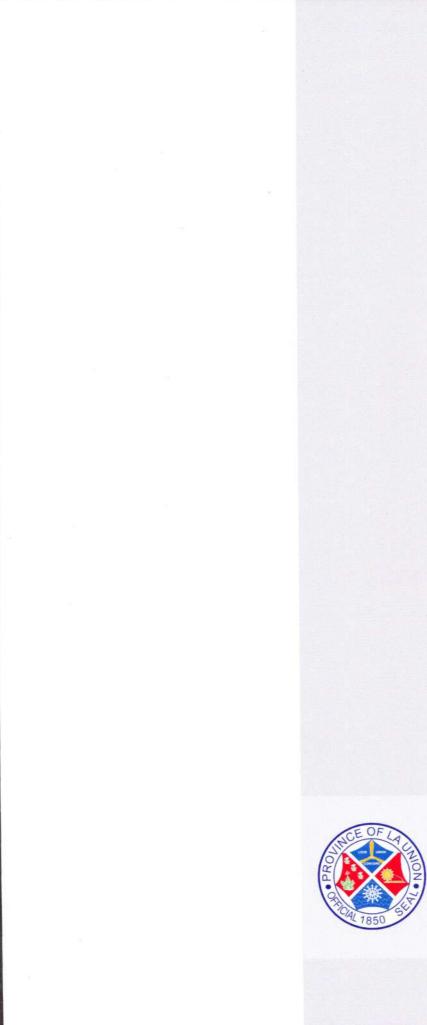



I
